



**KLUTINA RIVER AT
COPPER CENTER**

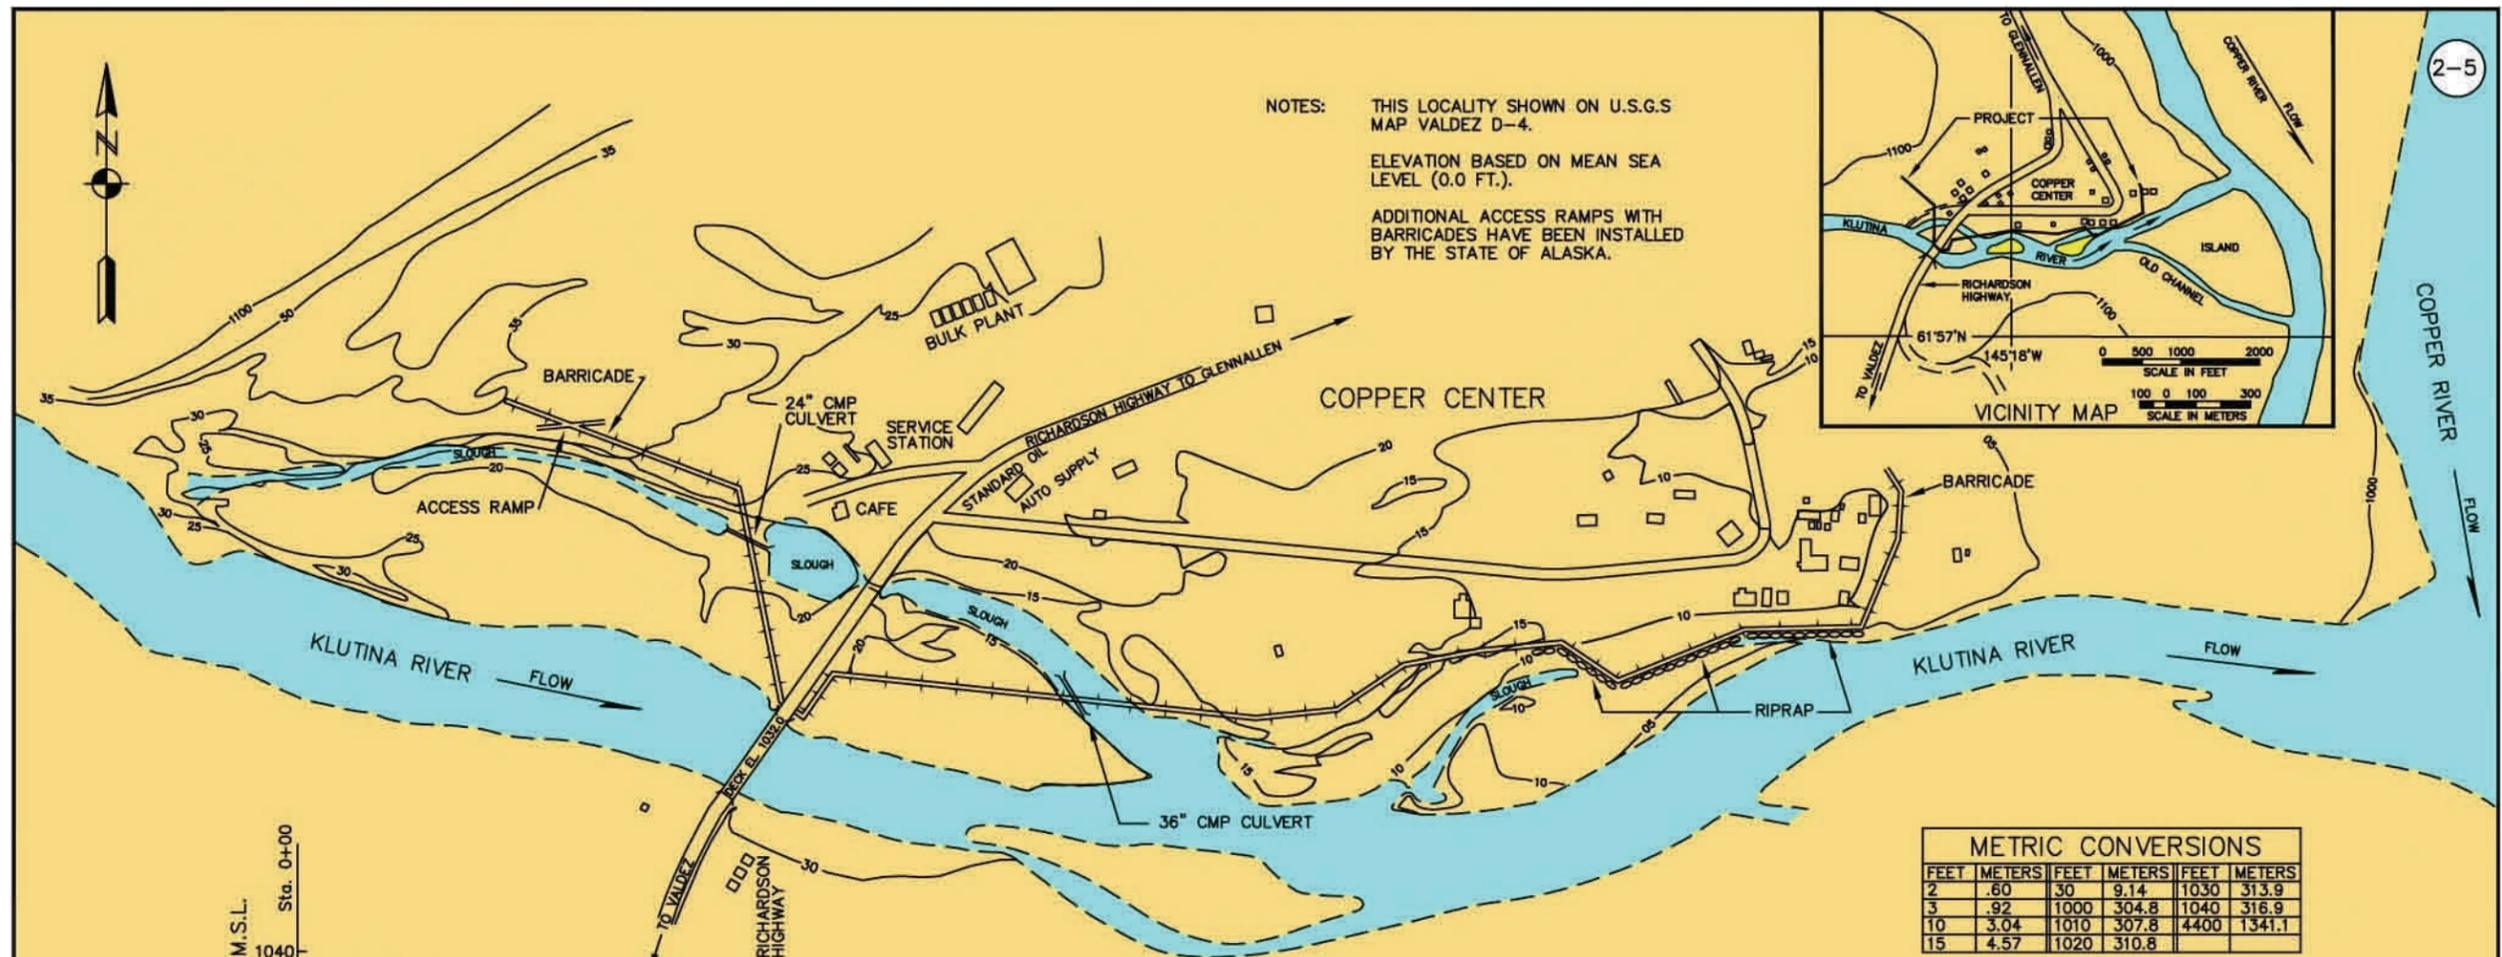


NOTES: THIS LOCALITY SHOWN ON U.S.G.S MAP VALDEZ D-4.
 ELEVATION BASED ON MEAN SEA LEVEL (0.0 FT.).
 ADDITIONAL ACCESS RAMPS WITH BARRICADES HAVE BEEN INSTALLED BY THE STATE OF ALASKA.


FEET	METERS	FEET	METERS	FEET	METERS
2	.60	30	9.14	1030	313.9
3	.92	1000	304.8	1040	316.9
10	3.04	1010	307.8	4400	1341.1
15	4.57	1020	310.8		

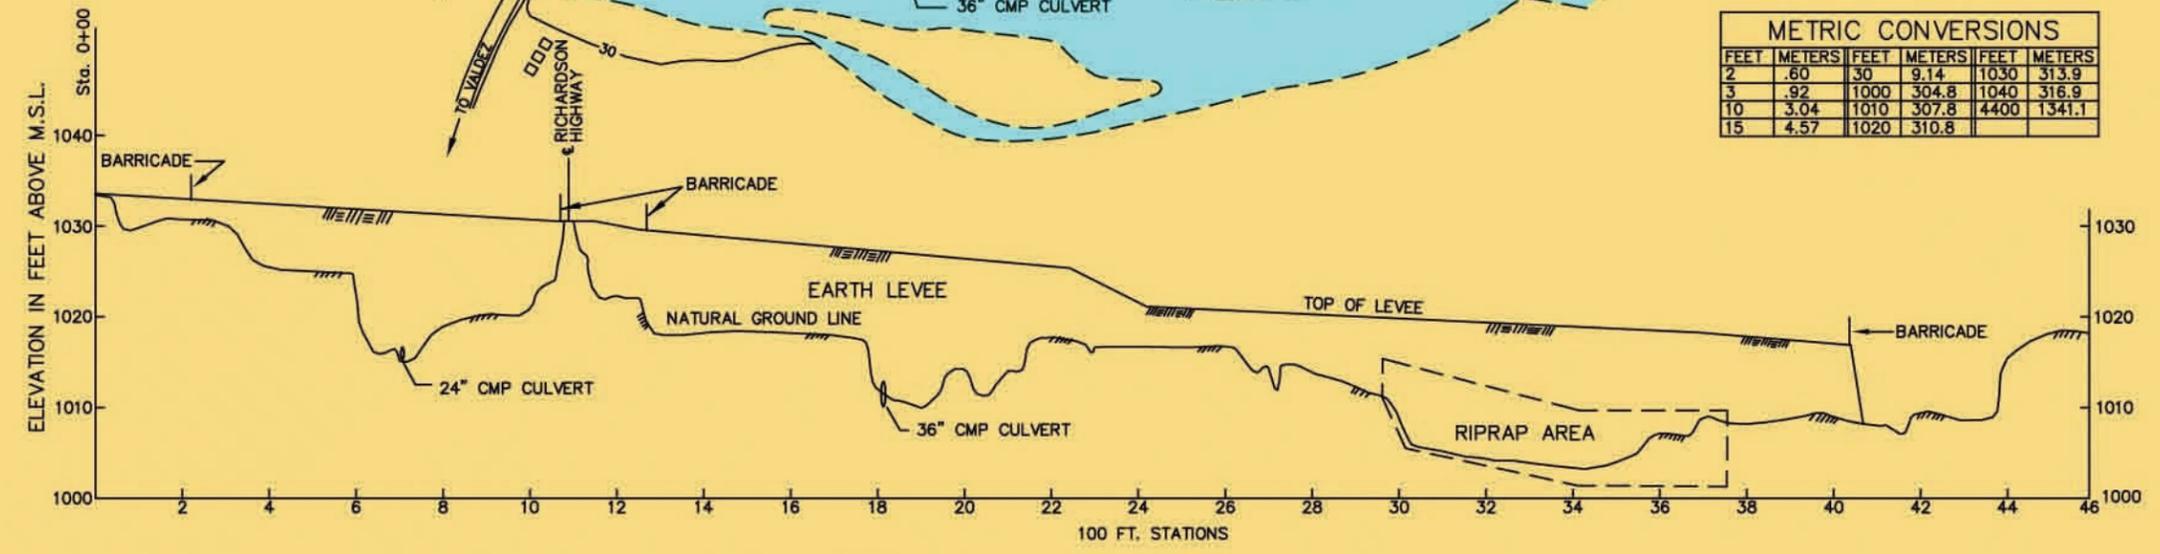

PROFILE ON CENTER LINE OF LEVEE




TYPICAL SECTION
NOT TO SCALE

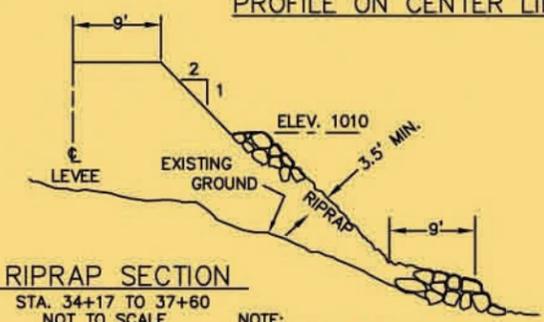


RIPRAP SECTION
STA. 34+17 TO 37+60
NOT TO SCALE

NOTE: REMAINDER OF RIPRAP AREA IDENTICAL EXCEPT FOR TOP ELEVATION.



TYPICAL ACCESS RAMP
NOT TO SCALE

FLOOD CONTROL
 KLUTINA RIVER
 ALASKA
 REVISED 1993



KLUTINA RIVER at COPPER CENTER, ALASKA

Condition of Improvement 30 September 2009

AUTHORIZATION: Flood Control Act, 30 June 1958, adopted as amended under Section 205, and authorized by the Chief of Engineers, 12 June 1968, provides for a levee 4,400 feet in length along the north bank of the Klutina River to protect the developed area of Copper Center and the northerly approach to the Richardson Highway bridge.

EXISTING PROJECT:	<u>LENGTH</u>	<u>HEIGHT</u>	<u>WIDTH</u>
• Levee	4100 ft	10 ft	10 ft
		avg	at top


PROJECT USAGE: This project provides flood protection for the developed area of Copper Center and the northerly Richardson Highway approach to the bridge crossing the Klutina River.

PROGRESS OF WORK:

- 1970 - The final design calls for a revised levee length of 4,100 feet with an average height of 10 feet and a top width of 10 feet. All costs in excess of \$1 million are to be funded by local interests.
- 1971 - Work on the levee begins in August and continues until suspended for the winter in October.
- 1972 - Construction is resumed in June and the project is deemed complete after a final inspection in August. The project is turned over to local interests for maintenance. Annual inspections determine compliance with the requirements of local cooperation.
- 1999 - The most recent inspection in July finds the project to be in satisfactory condition. A cut at station 8+50 has been filled requiring a local roadway to pass over the levee.
- 2000 - Inspection by Corps' personnel finds no deficiencies in the project.
- 2001 - The Corps' inspector reports that the project is in excellent condition.
- 2002 - The project is found in good condition. Recommendations are made to clear the levee of brush and keep the culverts free of debris.
- 2003 - The Corps' inspector describes the project as being in "great shape," June 2003.
- 2004 - Corps inspector finds 150 feet of revetment at the up-stream approach to the Richardson Highway bridge to be eroded and in need of new armor rip-rap. The embankment itself has been breached by a pedestrian walkway and two unauthorized barricades have been erected; these deficiencies need to be corrected by local interests.
- 2005 - The Corps inspector finds the project in good overall condition. The scour at the highway bridge abutment needs to be monitored so that the levy is not compromised. Repair to one culvert is recommended.
- 2009 - This project was inspected in June by USACE and the State of Alaska, DOT and Public Facilities.

COST TO DATE:	<u>New Work</u>	<u>Maintenance</u>	<u>Total</u>
	\$ 260,681	\$ 7,041	\$ 267,722

Klutina River, Copper Center, Alaska

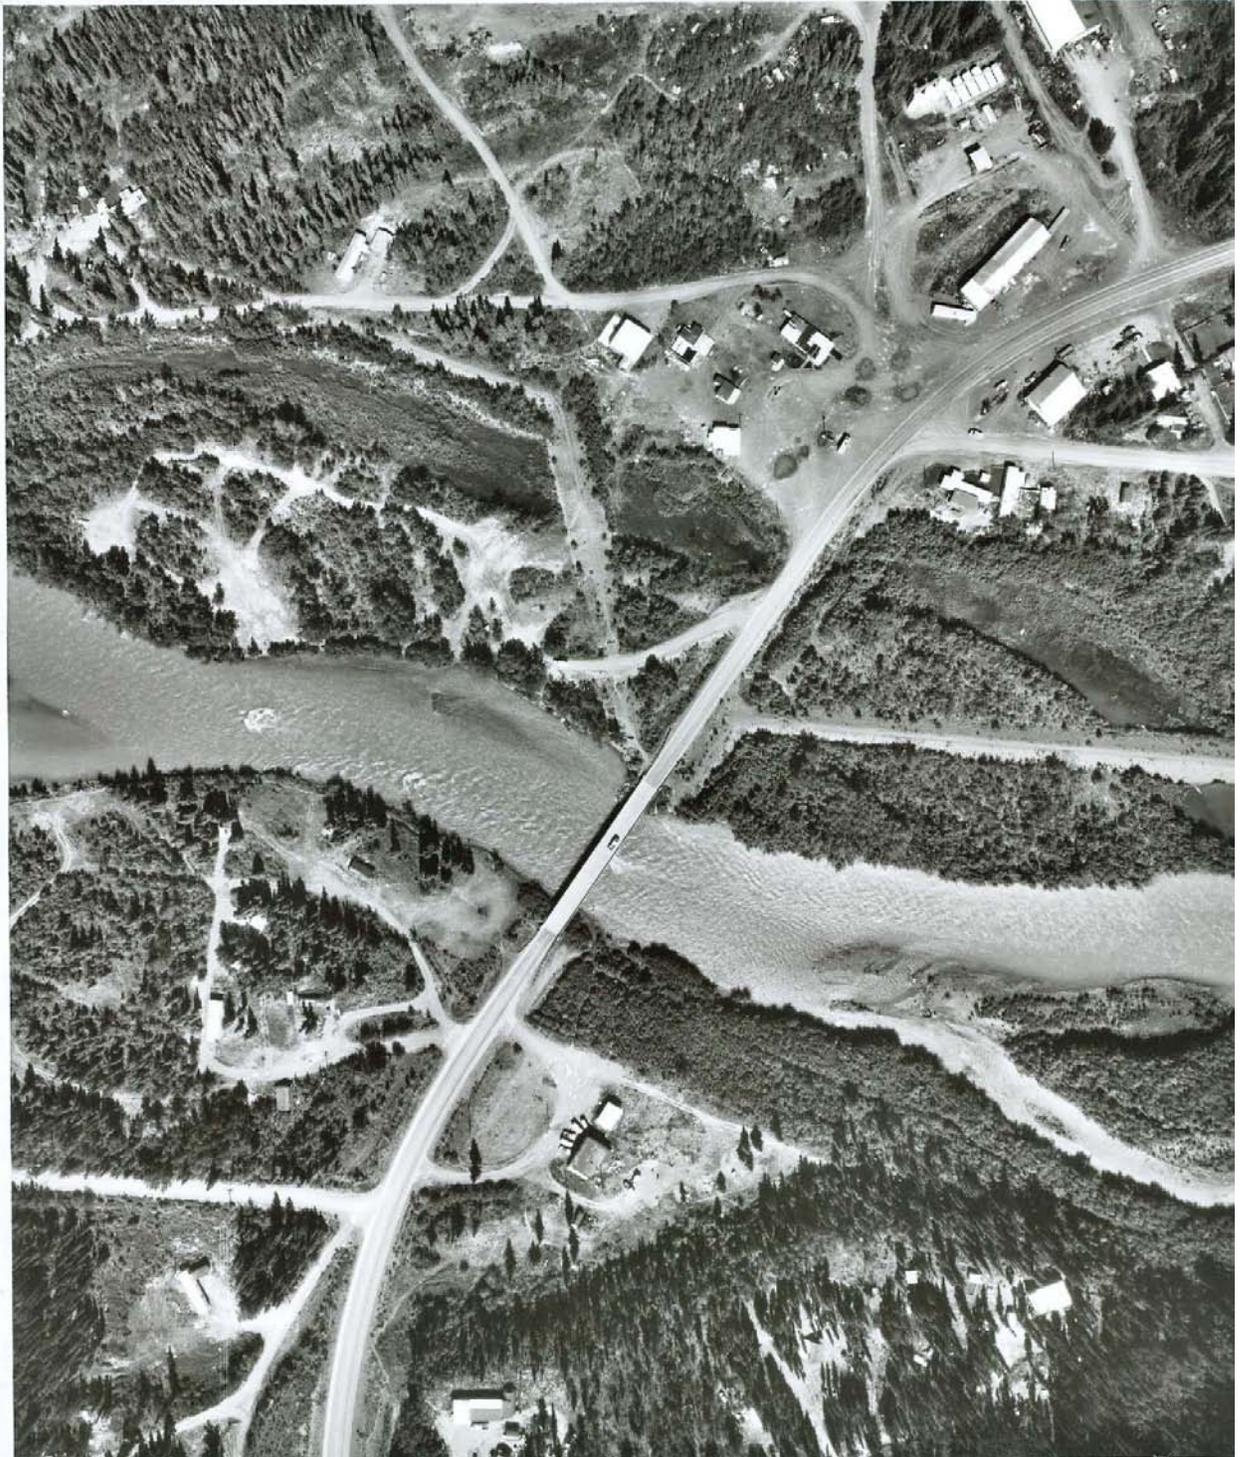

Aerial photo of the Klutina River
