# **Valdez New Harbor**

Valdez New Harbor Page 2 of 6

## Condition of Improvements 31 December 2022 Valdez New Harbor, Alaska

(CWIS No. 010600)

**Authorization** Water Resources Development Act of 2007, Section 4012, Public Law 110-114 provides for a new harbor adjacent Hotel Hill and east of the existing harbor. The project includes a 460 feet long stub breakwater, a 1,850 feet long detached breakwater, and 1,000 feet long east breakwater. These three sections of rubble mound breakwaters protect the new 14 acre basin with an entrance channel dredged to -18.5 feet MLLW and a maneuvering channel varying in dredged depth from -18.5 feet to -13.5 feet MLLW.

Table 1

<b>Existing Project</b>	Length ft.	Width ft.	Depth ft.
Basin (local)	637	275	-18.5
Basin (local)	730	330	-13.5
Entrance Channel	1065	130	-18.5
Maneuvering Channel	750	100	-18.5
Maneuvering Channel	750	100/75	-13.5
Stub Breakwater	525		
South Breakwater	1810		
East Breakwater	985		

**Project Usage** The New Valdez small boat harbor provides protected moorage for local and transient commercial fishing vessels as well as recreational craft. Valdez is located at the terminus of the trans-Alaska pipeline and is accessible by sea, air, and the Alaska Highway system.

#### **Progress of Work**

2015	A project condition survey of the existing harbor was completed in July. A contract
	for the new harbor is awarded and rock production begins.
2016	Construction continues with building of the breakwaters and dredging of basin.

Valdez New Harbor Page 3 of 6

#### **Progress of Work**

2017	Construction of the New harbor south of Hotel Hill is completed. A dredge
	verification survey was completed by eTRAC in September for the Alaska District.
2021	A project condition survey of the harbor was completed in May.

**Table 2 Cost to Date** 

Project	Description	Cost \$
010600	GI PED Appropriations	601,727
	GI PED Costs	662,883
	GI PED Contributed Appropriations	199,547
	GI PED Contributed Costs	75,532
	CG Appropriations	20,782,858
	CG Costs	18,392,939
	CG Contributed Appropriations	4,534,716
	CG Contributed Costs	4,534,716

Table 3 Range of Tides in feet

Tide Station	Mean Range	Diurnal Range	Extreme Range
945 4240 Valdez, Prince William Sound AK	9.70	12.15	22.50

NOAA Publication Date: 09/30/2011

**Controlling Depth** In May 2021, the controlling depth of -18.5 feet MLLW can be found throughout the entrance channel. Both of the Local Basins were dredged to required depths of -18.5 and -13.5.

### **Dredging Supplement**

#### A. Disposal

1. Dredge spoils were transported and discharged in a permitted deep water (-600') site approximately ¼ of a mile off shore in the port of Valdez.

#### **B.** Sampling and Testing

Valdez New Harbor Page 4 of 6

**Table 4 Chemical Testing** 

Method	Chemical analysis	Results
8080	Pesticides and PCB's	ND (none detedted)
Series 6000-7000's	(8) RCRA Metals	(4) of (8) detected; Mercury 14 - 21 ppm, all others below management thresholds
415.1	Total Organic Carbon	0.48 - 1.09 %
305.2	Ammonia as Nitrogen	2.2 - 19 ppm
9030	Total Sulfides	15 - 2500 ppm
160.1	Percent Solids	46.5 - 65.2 %
8260	Volatile Organic Compounds	ND or below management levels
8270	Semi-volatile Organics	Chrysene ND - 2.63 ppm, Fluoranthene ND - 5.61 ppm, Phenanthrene ND - 2.98 ppm, all others below management levels or ND


## C. Environmental Reports and Permits

**Table 5 Environmental Reports and Permits** 


Description	<b>Date of Issue</b>	<b>Date of Expiration</b>
Interim Feasibility Report and Environmental Assessment	May 2011	n/a
Findings of No Significant Impact	4-Oct-10	n/a
Updated Findings of No Significant Impact	26-Aug-14	n/a
ADEC Water Quality Certification	18-Sep-14	18-Sep-19
Fish and Wildlife Coordination Act Report	Sep 2006	n/a

Valdez New Harbor Page 5 of 6

# **Valdez New Harbor, Valdez Alaska**

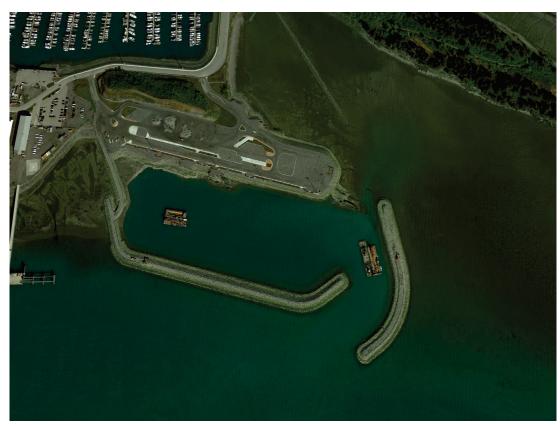

Valdez New Harbor Aerial View, May 2017

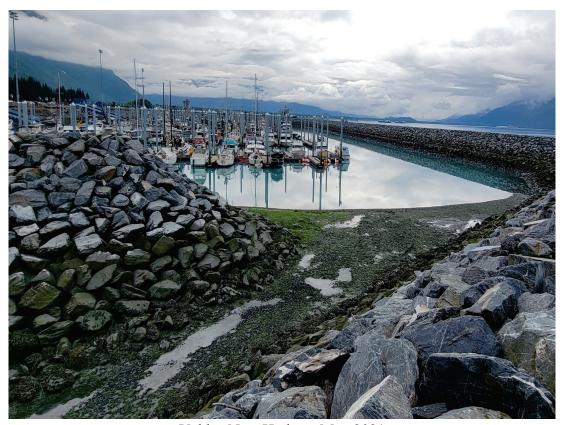

Valdez New Harbor, May 2021

Valdez New Harbor Page 6 of 6
